


Transmission Restoration Progress Report – As of March 28, 2018

- Overall progress on transmission line restoration is 75%, calculated as completed line segments divided by total line segments
- Progress on structure and component repair is 71%

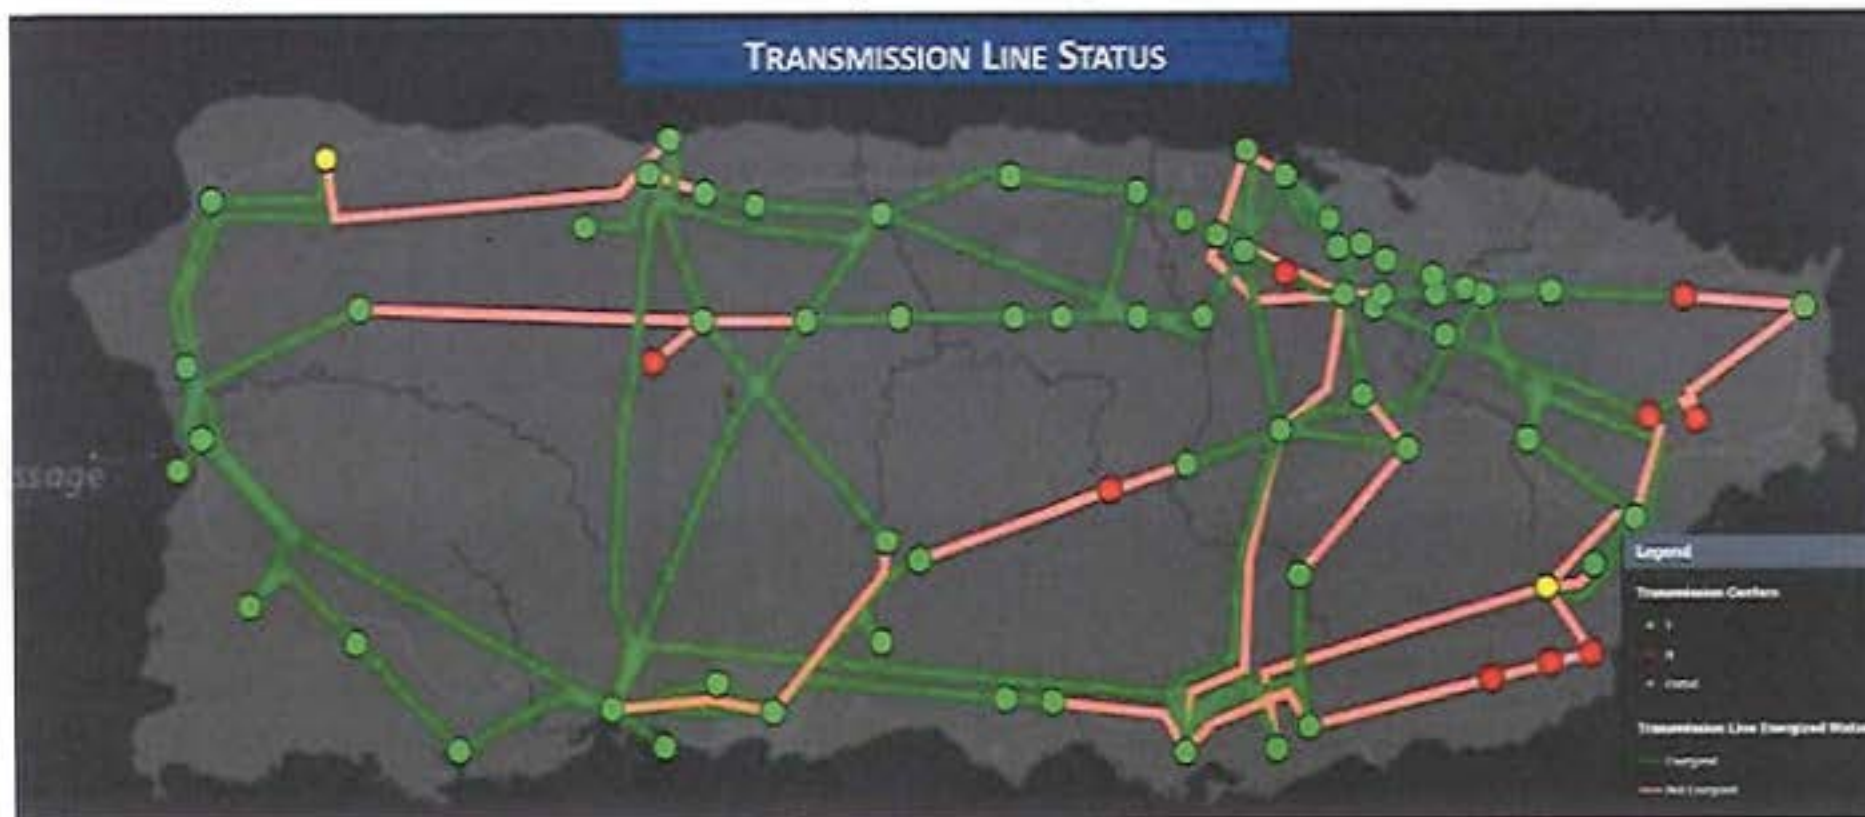

75%

OVERALL PROGRESS
(As per completedTasks)

TOTALS BY KV

(kV)	LINE SEGMENT	COMPLETED
230	17	14
115	86	63
Totals	103	77

TOTALS BY RESOURCE

	LINE SEGMENT	COMPLETED
PREPA	58	55
WHITEFISH	5	5
COBRA	12	4
NYPA	3	3
Fluor/PIKE	6	6
Fluor/ARC	1	1
Fluor/MasTec	0	0
Fluor/SEC	1	1
USACE/PowerSecure	3	2
Pending	14	0
Totals	103	77

	STRUCTURES (Towers/Poles)		DAMAGES (Conductors/Insulators)		Overall Repairs/Restoration %
(kV)	DOWN	REPAIRED	DEFICIENCY	REPAIRED	
230	107	103	404	317	82%
115	648	420	833	578	67%
Totals	755	523	1237	895	71%



Puerto Rico
Electric Power
Authority
